



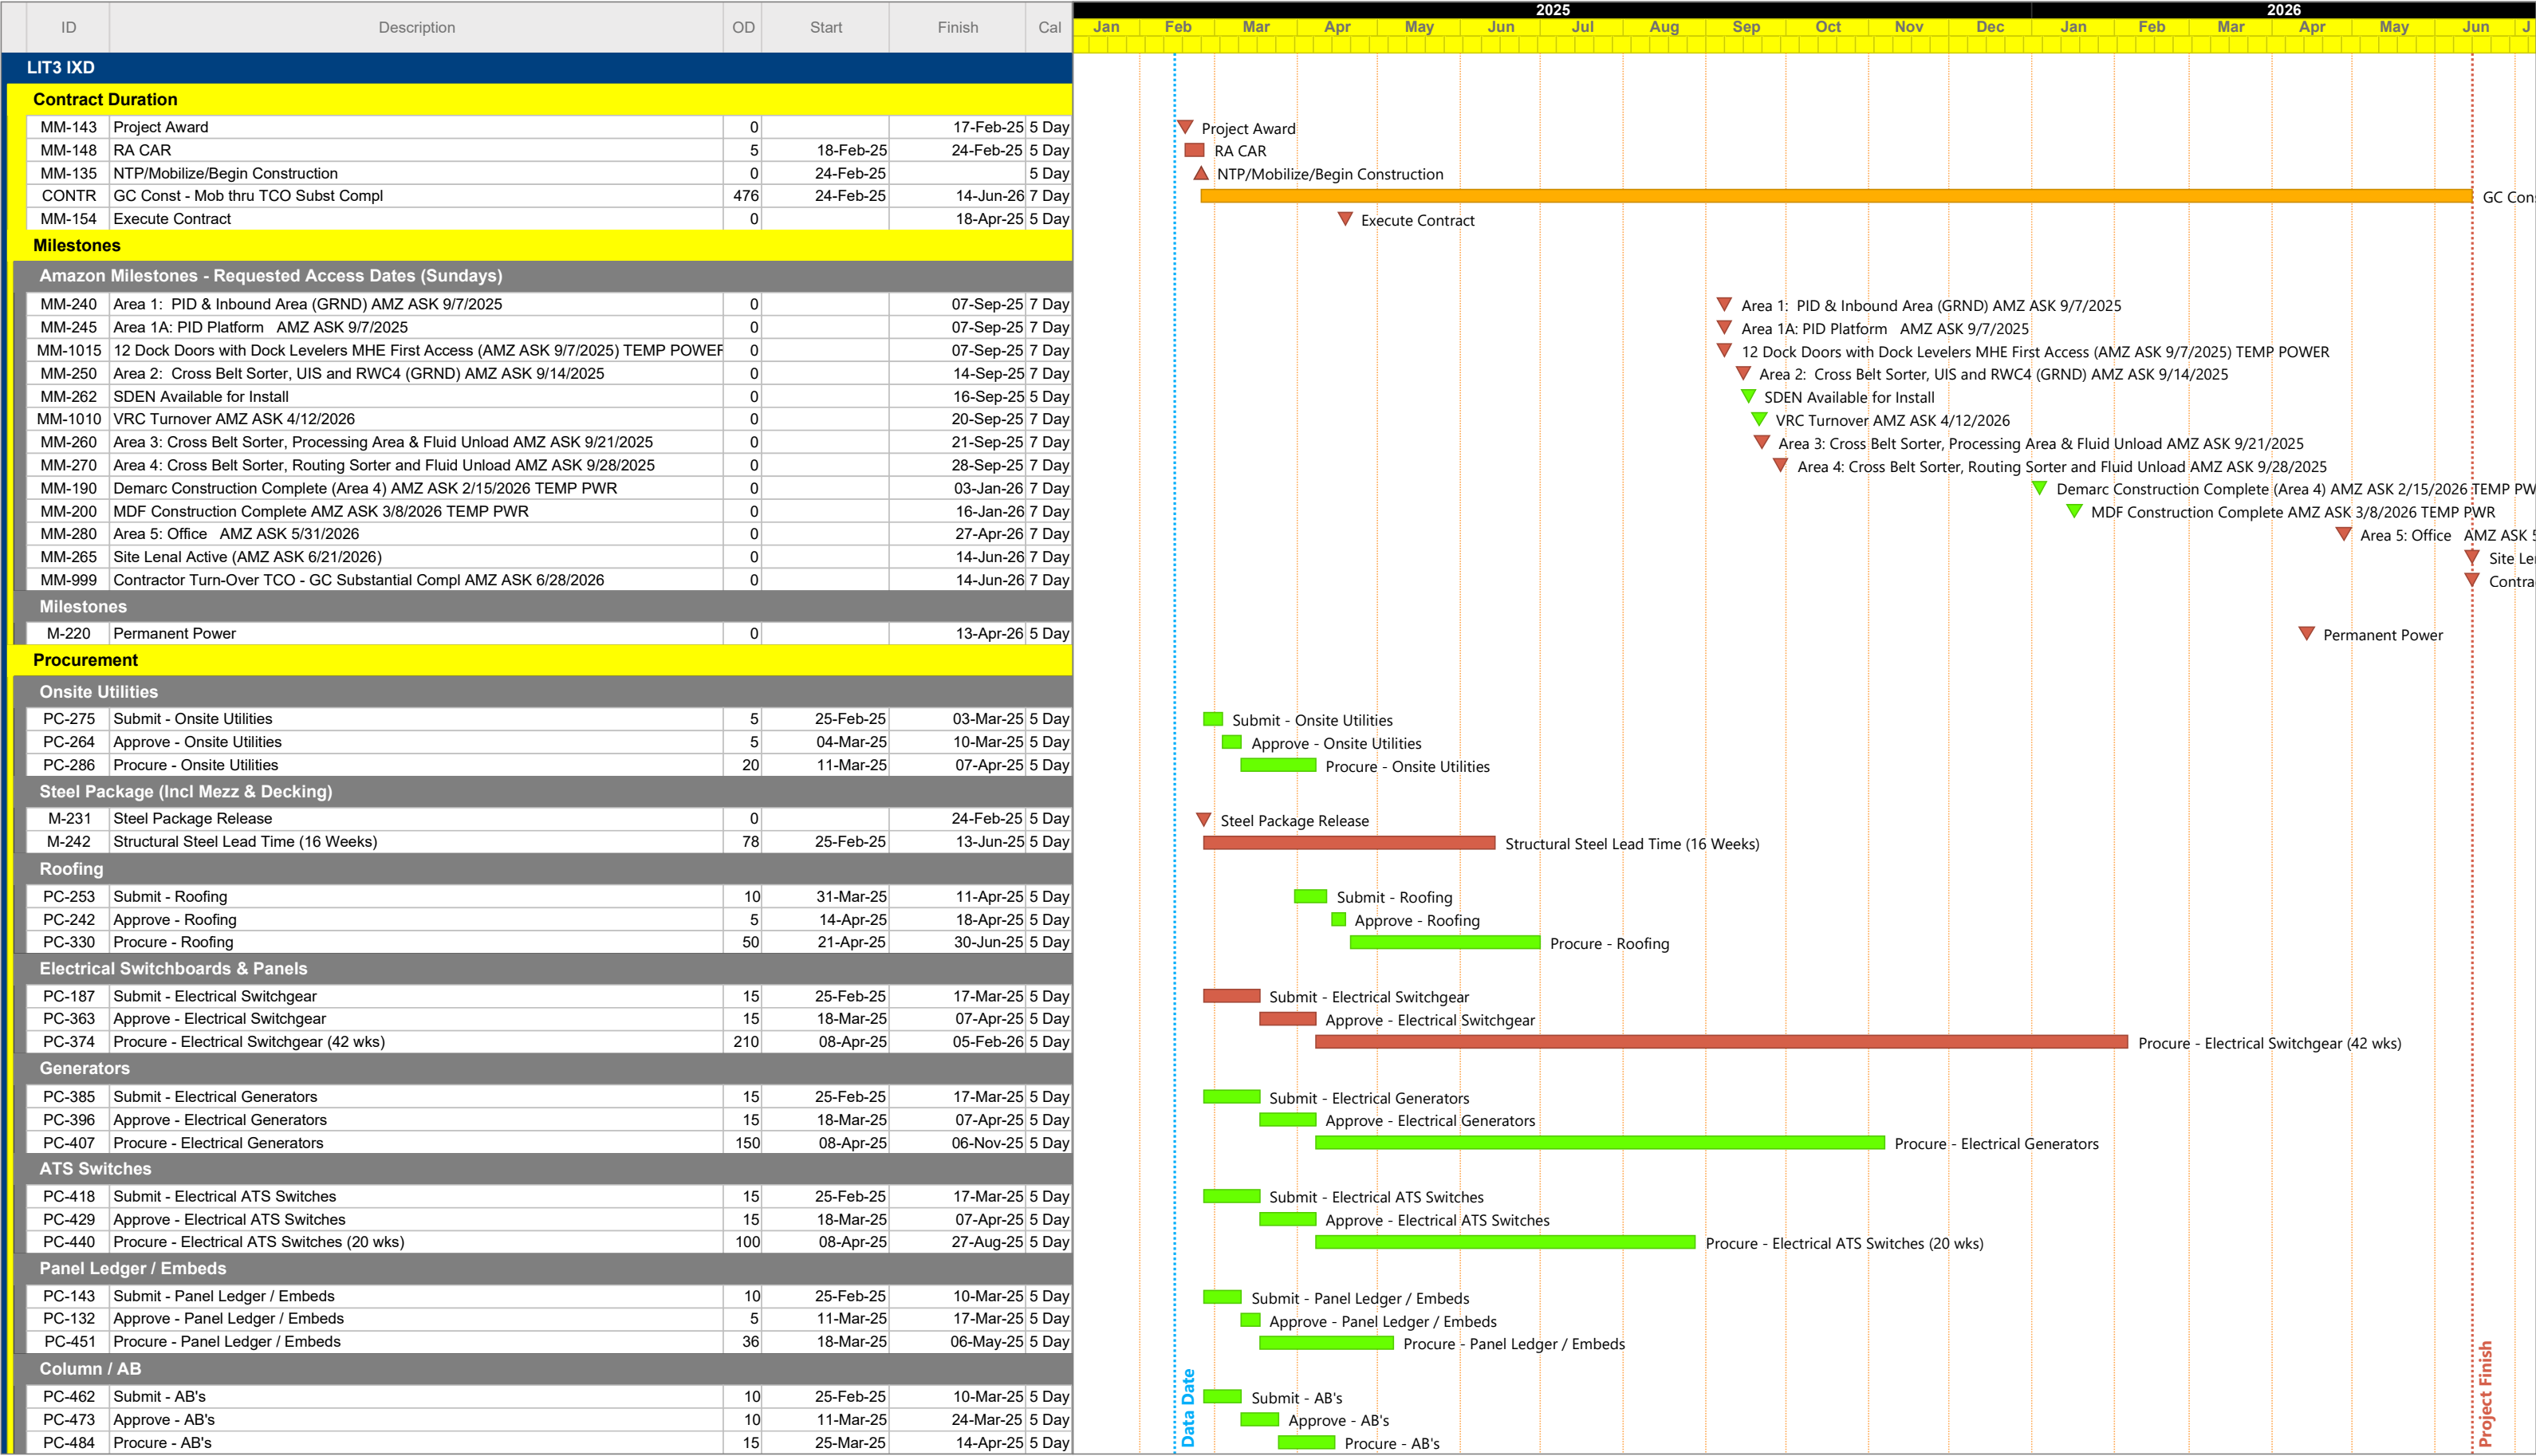

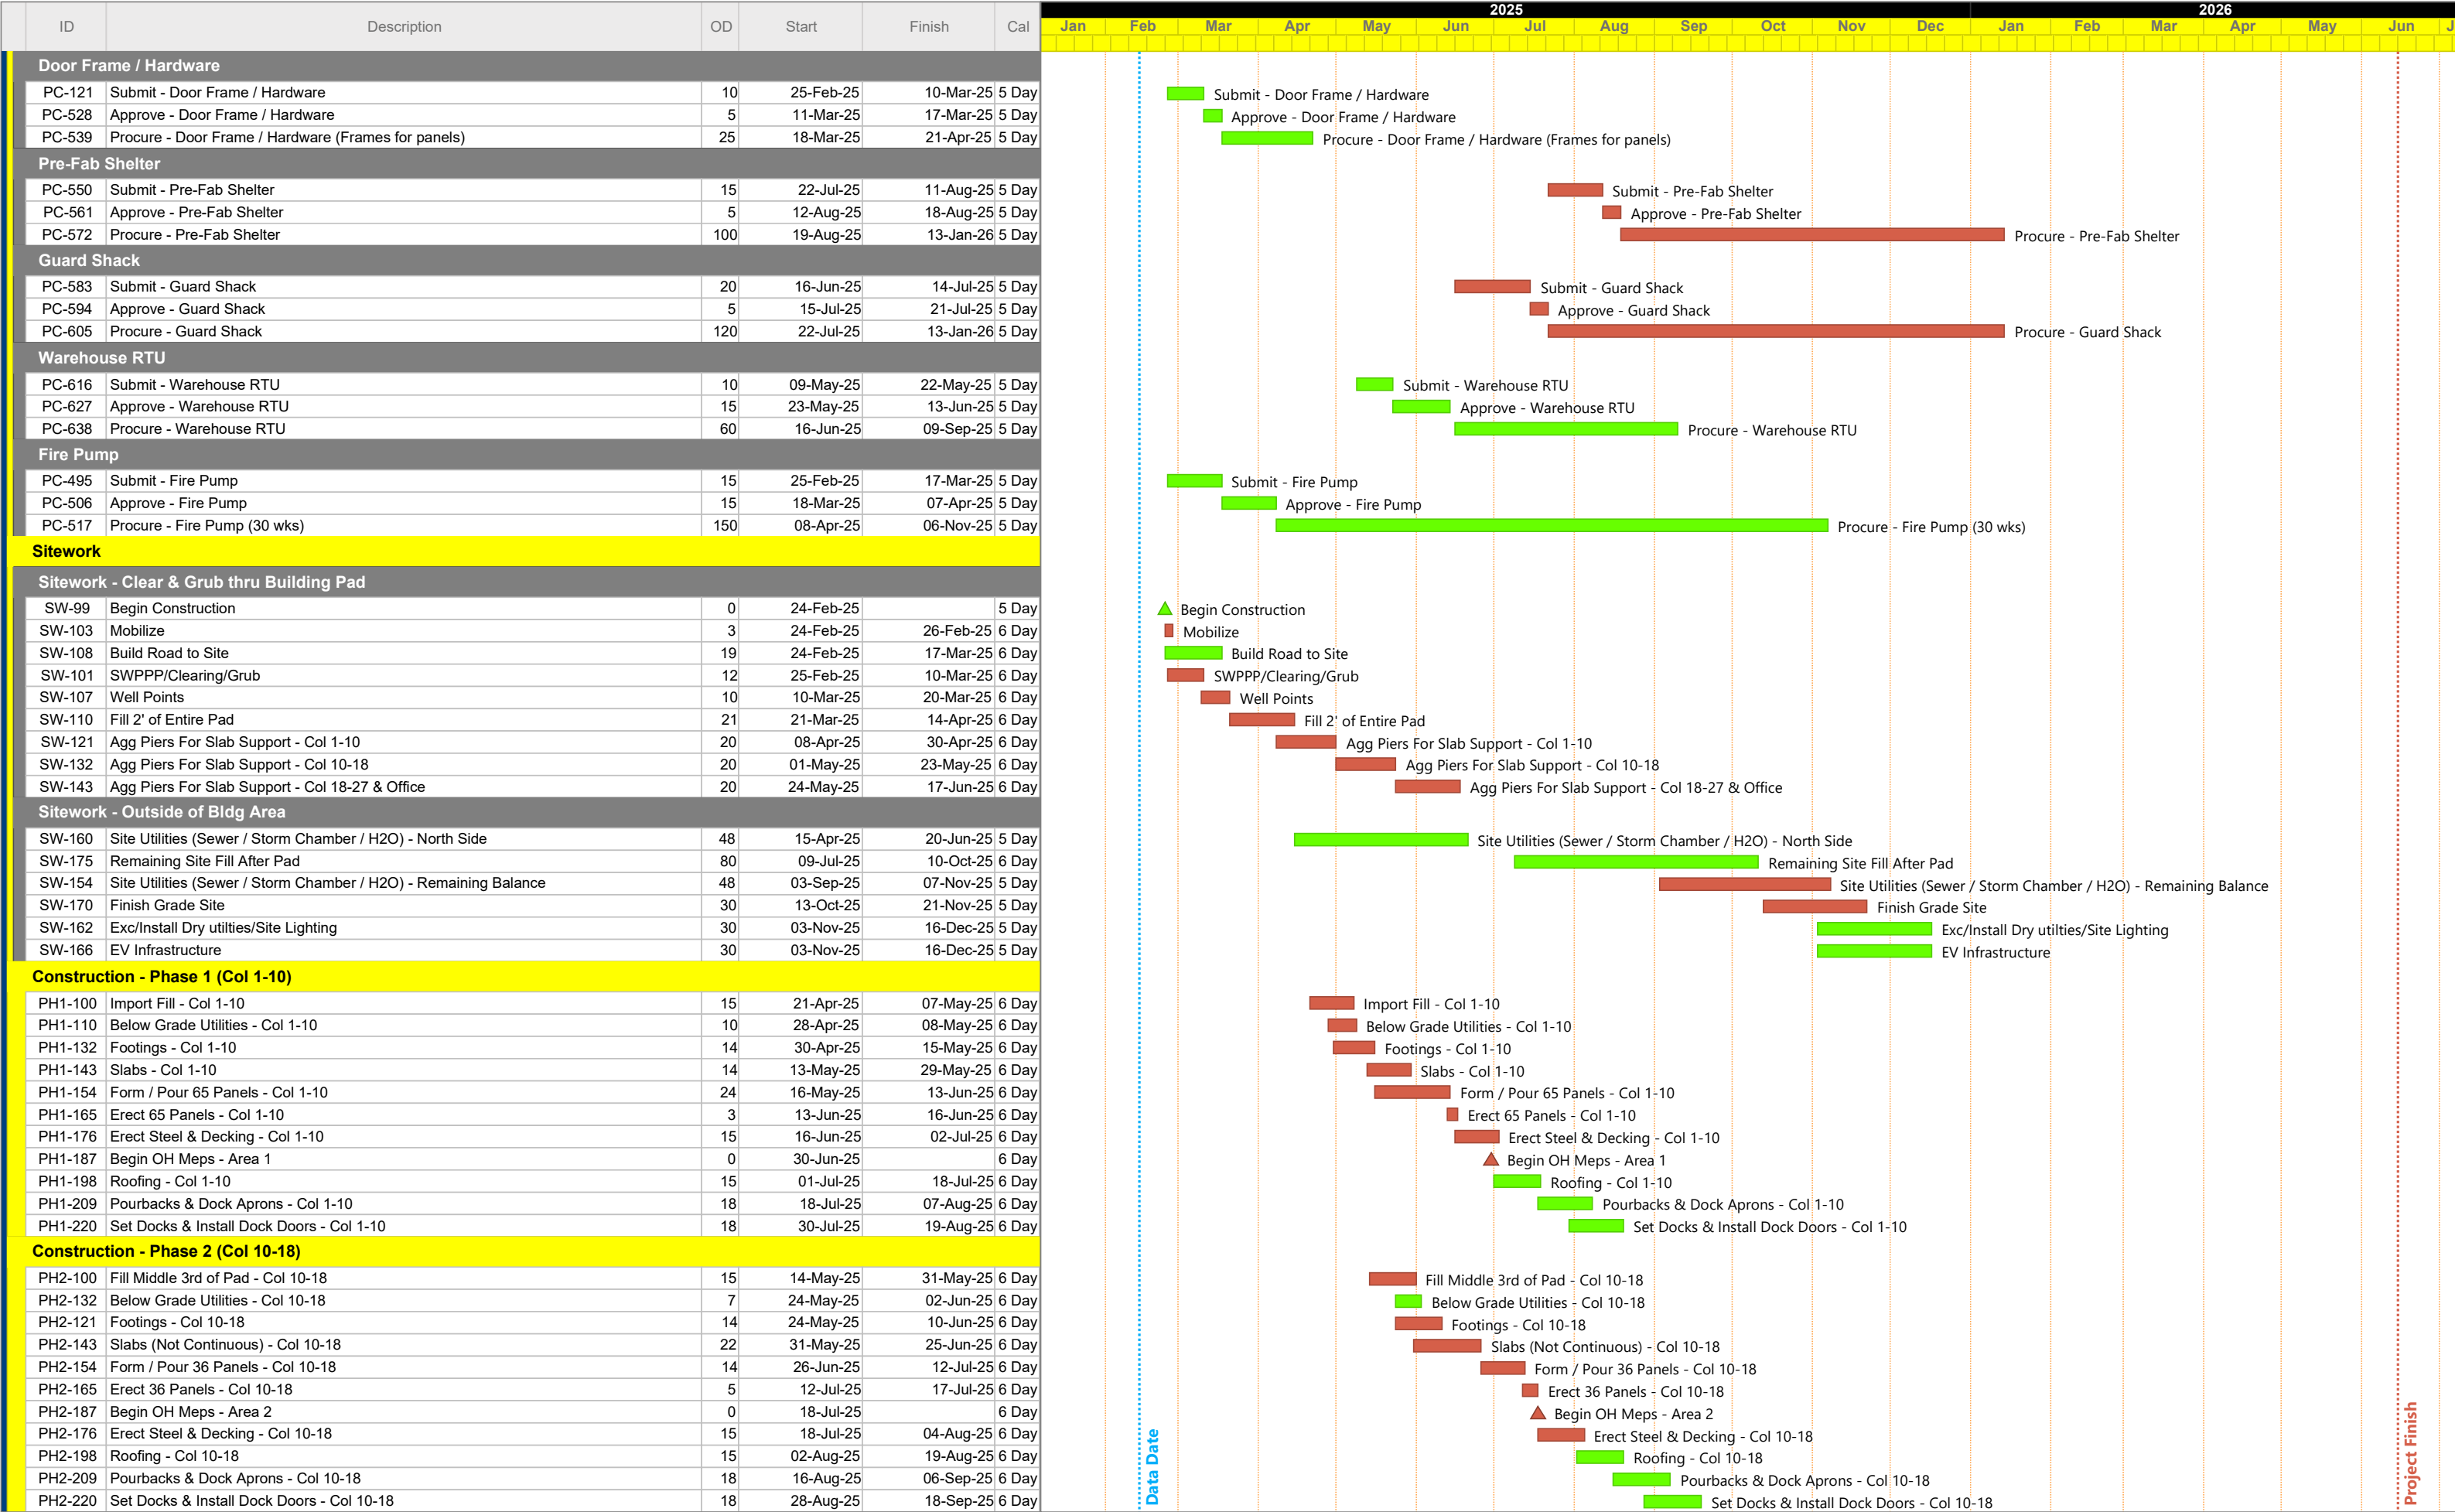

		2025												2026											
ID	Description	OD	Start	Finish	Cal	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	J	
Construction - Phase 3 (Col 18-27)																									
PH3-100	Fill Last 3rd of Pad - Col 18-27	15	09-Jun-25	25-Jun-25	6 Day																				
PH3-143	Below Grade Utilities - Col 18-27	7	19-Jun-25	26-Jun-25	6 Day																				
PH3-121	Footings (Not Continuous) - Col 18-27	20	19-Jun-25	12-Jul-25	6 Day																				
PH3-132	Slabs (Not Continuous) - Col 18-27	20	24-Jun-25	17-Jul-25	6 Day																				
PH3-154	Form / Pour Panels & Cure (Not Continuous) - Col 18-27	29	12-Jul-25	14-Aug-25	6 Day																				
PH3-176	Begin OH Meps - Area 3	0	05-Aug-25		5 Day																				
PH3-165	Erect Panels - Col 18-27	5	14-Aug-25	19-Aug-25	6 Day																				
PH3-187	Erect Steel & Decking - Col 18-27	15	14-Aug-25	30-Aug-25	6 Day																				
PH3-209	Begin OH Meps - Area 4	0	22-Aug-25		5 Day																				
PH3-198	Roofing - Col 18-27	15	29-Aug-25	16-Sep-25	6 Day																				
PH3-220	Pourbacks & Dock Aprons - Col 18-27	18	13-Sep-25	03-Oct-25	6 Day																				
PH3-231	Set Docks & Install Dock Doors - Col 18-27	18	25-Sep-25	15-Oct-25	6 Day																				
Construction - Office (Col 27-29)																									
OFC-100	Fill Office Pad - Col 27-29	10	26-Jun-25	08-Jul-25	6 Day																				
OFC-121	Form / Pour 32 Panels & Cure (Casting Beds) - Col 27-29	15	09-Jul-25	25-Jul-25	6 Day																				
OFC-132	Footings - Col 27-29	4	14-Jul-25	17-Jul-25	6 Day																				
OFC-143	Erect Panels - Col 27-29	2	25-Jul-25	26-Jul-25	6 Day																				
OFC-154	Below Grade Utilities - Col 27-29	7	28-Jul-25	04-Aug-25	6 Day																				
OFC-165	Erect Steel & Decking - Col 27-29	10	02-Sep-25	12-Sep-25	6 Day																				
OFC-176	Roofing - Col 27-29	6	17-Sep-25	23-Sep-25	6 Day																				
OFC-187	Slabs - Col 27-29	7	24-Sep-25	01-Oct-25	6 Day																				
OFC-198	Begin OH Meps	0	02-Oct-25		5 Day																				
Exterior / Enclosure																									
A1-420	Set Roof Top Units	10	17-Sep-25	30-Sep-25	5 Day																				
A1-425	Storefront / Glass	25	17-Sep-25	21-Oct-25	5 Day																				
A1-429	Painting	35	22-Oct-25	11-Dec-25	5 Day																				
Rough-in's & Finishes																									
Demarc & MDF Rooms																									
Office - Demarc Room Complete																									
A5-620	Framing thru Finishes - Demarc Room - Office Area	30	17-Sep-25	28-Oct-25	5 Day																				
A5-625	Finishes/Testing with Power - Demarc	30	29-Oct-25	11-Dec-25	5 Day																				
A5-627	Punchlist/Commisisoning	10	12-Dec-25	29-Dec-25	5 Day																				
A5-640	*** Turnover to Owner - Demarc *** AMZ ASK 2/15/2026 TEMP PWR	0		03-Jan-26	7 Day																				
Office - MDF Room Complete																									
A5-660	Framing thru Finishes - MDF Room - Office Area	35	17-Sep-25	04-Nov-25	5 Day																				
A5-665	MEP / Low Voltage / Fire Sprinkler - MDF Room	35	05-Nov-25	29-Dec-25	5 Day																				
A5-670	Finishes/Testing with Power - MDF	10	30-Dec-25	13-Jan-26	5 Day																				
A5-680	*** Turnover to Owner - MDF *** AMZ ASK 3/8/2026 TEMP PWR	0		16-Jan-26	7 Day																				
Area 1																									
Area 1 - Interior & Rough-In																									
A1-100	Area 1 Rough-in's --> Turnover SUMMARY (6 day a week)	60	28-Jun-25	08-Sep-25	6 Day																				
A1-110	Fire Sprinklers - Area 1	18	30-Jun-25	21-Jul-25	6 Day																				
A1-121	Overhead Rough-In's - Area 1	12	11-Jul-25	24-Jul-25	6 Day																				
A1-198	Int Panel & Column Paint - Area 1	6	25-Jul-25	31-Jul-25	6 Day																				
A1-220	Panel Insulation - Area 1	6	25-Jul-25	31-Jul-25	6 Day																				
A1-143	Low Voltage Rough-In's - Area 1	10	25-Jul-25	05-Aug-25	6 Day																				
A1-154	Light Fixtures - Area 1	12	25-Jul-25	07-Aug-25	6 Day																				
A1-165	Mechanical Trim - Area 1	12	25-Jul-25	07-Aug-25	6 Day																				
A1-187	Low Voltage Trim - Area 1	6	02-Aug-25	08-Aug-25	6 Day																				
A1-209	Sawcut / Seal Joints - Area 1	6	09-Aug-25	15-Aug-25	6 Day																				
A1-231	Punchlist & Final Walk thru with Owner - Area 1	6	16-Aug-25	21-Aug-25	7 Day																				
A1-236	Weather Allowance - Area 1	17	22-Aug-25	07-Sep-25	7 Day																				
A1-242	*** Turnover to Owner - Area 1 *** AMZ ASK 9/7/2025	0		07-Sep-25	7 Day																				
Area 1 - TI																									
A1-640	TI - Remote Bathroom - Area 1	40	19-Aug-25	14-Oct-25	5 Day																				
A1-650	TI - Bathroom & Breakroom - Area 1	40	19-Aug-25	14-Oct-25	5 Day																				
Area 1A - Mezzanine																									
A1A-100	Mezzanine - SOMD Area 1	15	03-Jul-25	21-Jul-25	6 Day																				
A1A-110	Paint - Mezzanine Area 1	3	22-Jul-25	24-Jul-25	6 Day																				
A1A-121	Fire Sprinkler Under Mezzanine - Area 1	9	25-Jul-25	04-Aug-25	6 Day																				
A1A-132	MEP's Under Mezzanine - Area 1	11	01-Aug-25	13-Aug-25	6 Day																				

Data Date

Project Finish

						2025												2026											
ID	Description	OD	Start	Finish	Cal	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	J					
A1A-137	Weather Allowance - Area 1A	25	14-Aug-25	07-Sep-25	7 Day																								
A1-VRC1	VRC Install	20	14-Aug-25	11-Sep-25	5 Day																								
A1A-143	*** Turnover to Owner - Area 1 PID Platform *** 9/7/2025	0		07-Sep-25	7 Day																								
A1-VRC11	Punchlist / Corrections / Start-up / Commissioning	5	12-Sep-25	18-Sep-25	5 Day																								
A1-VRC22	*** Turnover to Owner - VRC *** AMZ ASK 4/12/2026	0		20-Sep-25	7 Day																								
Area 2																													
Area 2 - Interior & Rough-In																													
A2-100	Area 2 Rough-in's --> Turnover SUMMARY (6 day a week)	51	17-Jul-25	15-Sep-25	6 Day																								
A2-110	Fire Sprinklers - Area 2	18	18-Jul-25	07-Aug-25	6 Day																								
A2-121	Overhead Rough-In's - Area 2	12	25-Jul-25	07-Aug-25	6 Day																								
A2-198	Int Panel & Column Paint - Area 2	6	08-Aug-25	14-Aug-25	6 Day																								
A2-209	Panel Insulation - Area 2	6	08-Aug-25	14-Aug-25	6 Day																								
A2-132	Low Voltage Rough-In's - Area 2	10	08-Aug-25	19-Aug-25	6 Day																								
A2-143	Light Fixtures - Area 2	12	08-Aug-25	21-Aug-25	6 Day																								
A2-154	Mechanical Trim - Area 2	12	08-Aug-25	21-Aug-25	6 Day																								
A2-187	Low Voltage Trim - Area 2	6	16-Aug-25	22-Aug-25	6 Day																								
A2-220	Sawcut / Seal Joints - Area 2	6	23-Aug-25	29-Aug-25	6 Day																								
A2-231	Punchlist & Final Walk thru with Owner - Area 2	6	30-Aug-25	04-Sep-25	7 Day																								
A2-236	Weather Allowance - Area 2	8	05-Sep-25	12-Sep-25	7 Day																								
A2-242	*** Turnover to Owner - Area 2 *** AMZ ASK 9/14/2025	0		14-Sep-25	7 Day																								
Area 2 - TI																													
A2-650	TI - Remote Bathroom - Area 2	40	15-Oct-25	11-Dec-25	5 Day																								
A2-660	TI - Bathroom & Breakroom - Area 2	40	15-Oct-25	11-Dec-25	5 Day																								
Area 3																													
Area 2 - Interior & Rough-In																													
A3-100	Area 3 Rough-in's --> Turnover SUMMARY (6 day a week)	42	04-Aug-25	22-Sep-25	6 Day																								
A3-110	Fire Sprinklers - Area 3	18	05-Aug-25	25-Aug-25	6 Day																								
A3-121	Overhead Rough-In's - Area 3	12	15-Aug-25	28-Aug-25	6 Day																								
A3-209	Int Panel & Column Paint - Area 3	6	29-Aug-25	05-Sep-25	6 Day																								
A3-220	Panel Insulation - Area 3	6	29-Aug-25	05-Sep-25	6 Day																								
A3-132	Low Voltage Rough-In's - Area 3	10	29-Aug-25	10-Sep-25	6 Day																								
A3-143	Light Fixtures - Area 3	12	29-Aug-25	12-Sep-25	6 Day																								
A3-154	Mechanical Trim - Area 3	12	29-Aug-25	12-Sep-25	6 Day																								
A3-187	Low Voltage Trim - Area 3	6	08-Sep-25	13-Sep-25	6 Day																								
A3-198	Sawcut / Seal Joints - Area 3	6	08-Sep-25	13-Sep-25	6 Day																								
A3-231	Punchlist & Final Walk thru with Owner - Area 3	6	08-Sep-25	13-Sep-25	7 Day																								
A3-236	Weather Allowance - Area 2	8	14-Sep-25	21-Sep-25	7 Day																								
A3-242	*** Turnover to Owner - Area 3 *** AMZ ASK 9/21/2025	0		21-Sep-25	7 Day																								
Area 3 - TI																													
A3-620	TI - Remote Bathroom - Area 3	40	15-Oct-25	11-Dec-25	5 Day																								
A3-630	TI - Bathroom & Breakroom - Area 3	40	15-Oct-25	11-Dec-25	5 Day																								
Area 4																													
Area 4 - Interior & Rough-In																													
A4-100	Area 4 Rough-in's --> Turnover SUMMARY (6 day a week)	33	21-Aug-25	29-Sep-25	6 Day																								
A4-110	Fire Sprinklers - Area 4	18	22-Aug-25	12-Sep-25	6 Day																								
A4-121	Overhead Rough-In's - Area 4	12	29-Aug-25	12-Sep-25	6 Day																</								

