

1. CONTRACTOR IS SOLELY RESPONSIBLE FOR SELECTION, IMPLEMENTATION, MAINTENANCE, AND EFFECTIVENESS OF ALL SWPPP CONTROLS - CONTROLS SHOWN ON THIS SITE MAP ARE SUGGESTED CONTROLS ONLY.

2. CONTRACTOR SHALL RECORD INSTALLATION, MAINTENANCE OR MODIFICATION AND REMOVAL DATES FOR EACH BMP EMPLOYED (WHETHER CALLED OUT ON ORIGINAL SWPPP OR NOT) DIRECTLY ON THIS SITE MAP.

3. DRAINAGE PATTERNS ARE SHOWN ON THIS PLAN BY PROPOSED AND EXISTING CONTOURS.

4. TEMPORARY AND PERMANENT STABILIZATION PRACTICES AND BMP'S SHALL BE INSTALLED AT THE EARLIEST POSSIBLE TIME DURING THE CONSTRUCTION SEQUENCE. AS AN EXAMPLE, PERIMETER SILT FENCE SHALL BE INSTALLED PRIOR TO COMMENCEMENT OF ANY GRADING ACTIVITIES. OTHER BMP'S SHALL BE INSTALLED AS SOON AS PRACTICABLE AND SHALL BE MAINTAINED UNTIL FINAL SITE STABILIZATION IS ATTAINED. CONTRACTOR SHALL ALSO REFERENCE CIVIL PLAN FOR WHERE PERMANENT STABILIZATION IS PROVIDED BY LANDSCAPING AND SITE PAVING.

5. BMP'S HAVE BEEN LOCATED AS INDICATED ON THIS PLAN IN ACCORDANCE WITH GENERALLY ACCEPTED ENGINEERING PRACTICES IN ORDER TO MINIMIZE SEDIMENT TRANSFER, FOR EXAMPLE: SILT FENCES LOCATED AT TOE OF SLOPE AND INLET PROTECTION FOR INLETS RECEIVING SEDIMENT FROM SITE RUN-OFF.

6. SANITARY SEWER EFFLUENT IS DISPOSED OF VIA AN ONSITE SEWER SYSTEM CONNECTED TO A MUNICIPAL SEWER SYSTEM.

7. CONTRACTOR TO PROVIDE INLET PROTECTION IN PUBLIC ROW ONLY DURING EARTH MOVING ACTIVITIES. CONTRACTOR TO ENSURE PONDING DOES NOT OCCUR IN PUBLIC ROW OR ON ADJACENT PROPERTIES AT ANY TIME DURING CONSTRUCTION.

8. CONSTRUCTION ENTRANCE SHALL BE LOCATED SO AS TO PROVIDE THE LEAST AMOUNT OF DISTURBANCE TO THE FLOW OF TRAFFIC IN AND OUT OF THE SITE. ADDITIONALLY, THE CONSTRUCTION ENTRANCE SHALL BE LOCATED TO COINCIDE WITH THE PHASING OF THE PARKING LOT CONSTRUCTION.

9. CONTRACTOR SHALL PROVIDE INLET PROTECTION FOR ANY AFFECTED INLET DOWNSTREAM OF THE PROPOSED IMPROVEMENTS, IF NEEDED.

10. THE NATURE OF THIS SITE'S CONSTRUCTION CONSISTS OF CLEARING & SITE PREPARATION, EARTHWORK, PAVING AND LANDSCAPING.

11. SEDIMENTATION BASIN: NEITHER A TEMPORARY NOR PERMANENT SEDIMENTATION BASIN HAS BEEN PROVIDED ON THIS SITE BECAUSE THE SITE IS

12. POST CONSTRUCTION STORM WATER POLLUTION CONTROL MEASURES INCLUDE STABILIZATION BY PERMANENT PAVING AND LANDSCAPING.

13. DISTURBED PORTIONS OF SITE MUST BE STABILIZED. STABILIZATION PRACTICES MUST BE INITIATED WITHIN 14 DAYS IN PORTIONS OF THE SITE WHERE CONSTRUCTION HAS BEEN EITHER TEMPORARILY OR PERMANENTLY CEASED, UNLESS EXCEPTED WITHIN THE OPDES PERMIT. CONTRACTOR SHALL REMOVE TEMPORARY EROSION CONTROL DEVICES UPON COMPLETION OF STABILIZATION.

14. CONTRACTOR IS RESPONSIBLE FOR MODIFYING THE SWPPP/SITE MAP TO INCLUDE BMP'S FOR ANY OFF-SITE MATERIAL WASTE, BORROW OR EQUIPMENT STORAGE AREAS.

15. CONTRACTOR IS RESPONSIBLE FOR SUBMITTAL OF NOI, NOT, POSTING OF S
NOTICES, AND ANY ADDITIONAL INFORMATION OR SUBMITTALS REQUIRED BY A
EPA, OR LOCAL JURISDICTION.

16. CONTRACTOR TO MAINTAIN NO MORE THAN 10 ACRES OF DRAINAGE TO ANY SINGLE OUTFALL LOCATION DURING CONSTRUCTION.

1	01/23/2028	DESIGN DEVELOPMENT
---	------------	--------------------

--	--	--

--	--	--	--


This document is incomplete and may not be used for regulatory approval, permit or construction.

Date of issue:

Date of Issue:	01/23/2026
----------------	------------

SERVERFARM - ARK01
DESIGN DEVELOPMENT


Clarksville, AR 72830

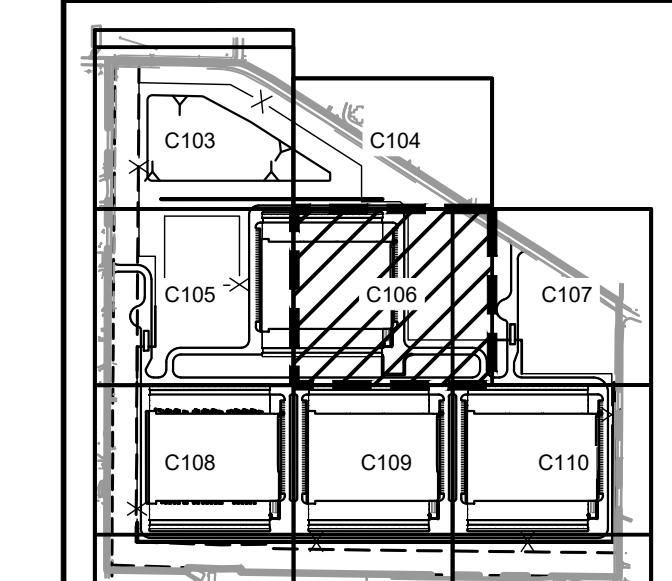

EROSION
CONTROL PLAN
(4 OF 8)

JOB 065011204
SHEET

C106

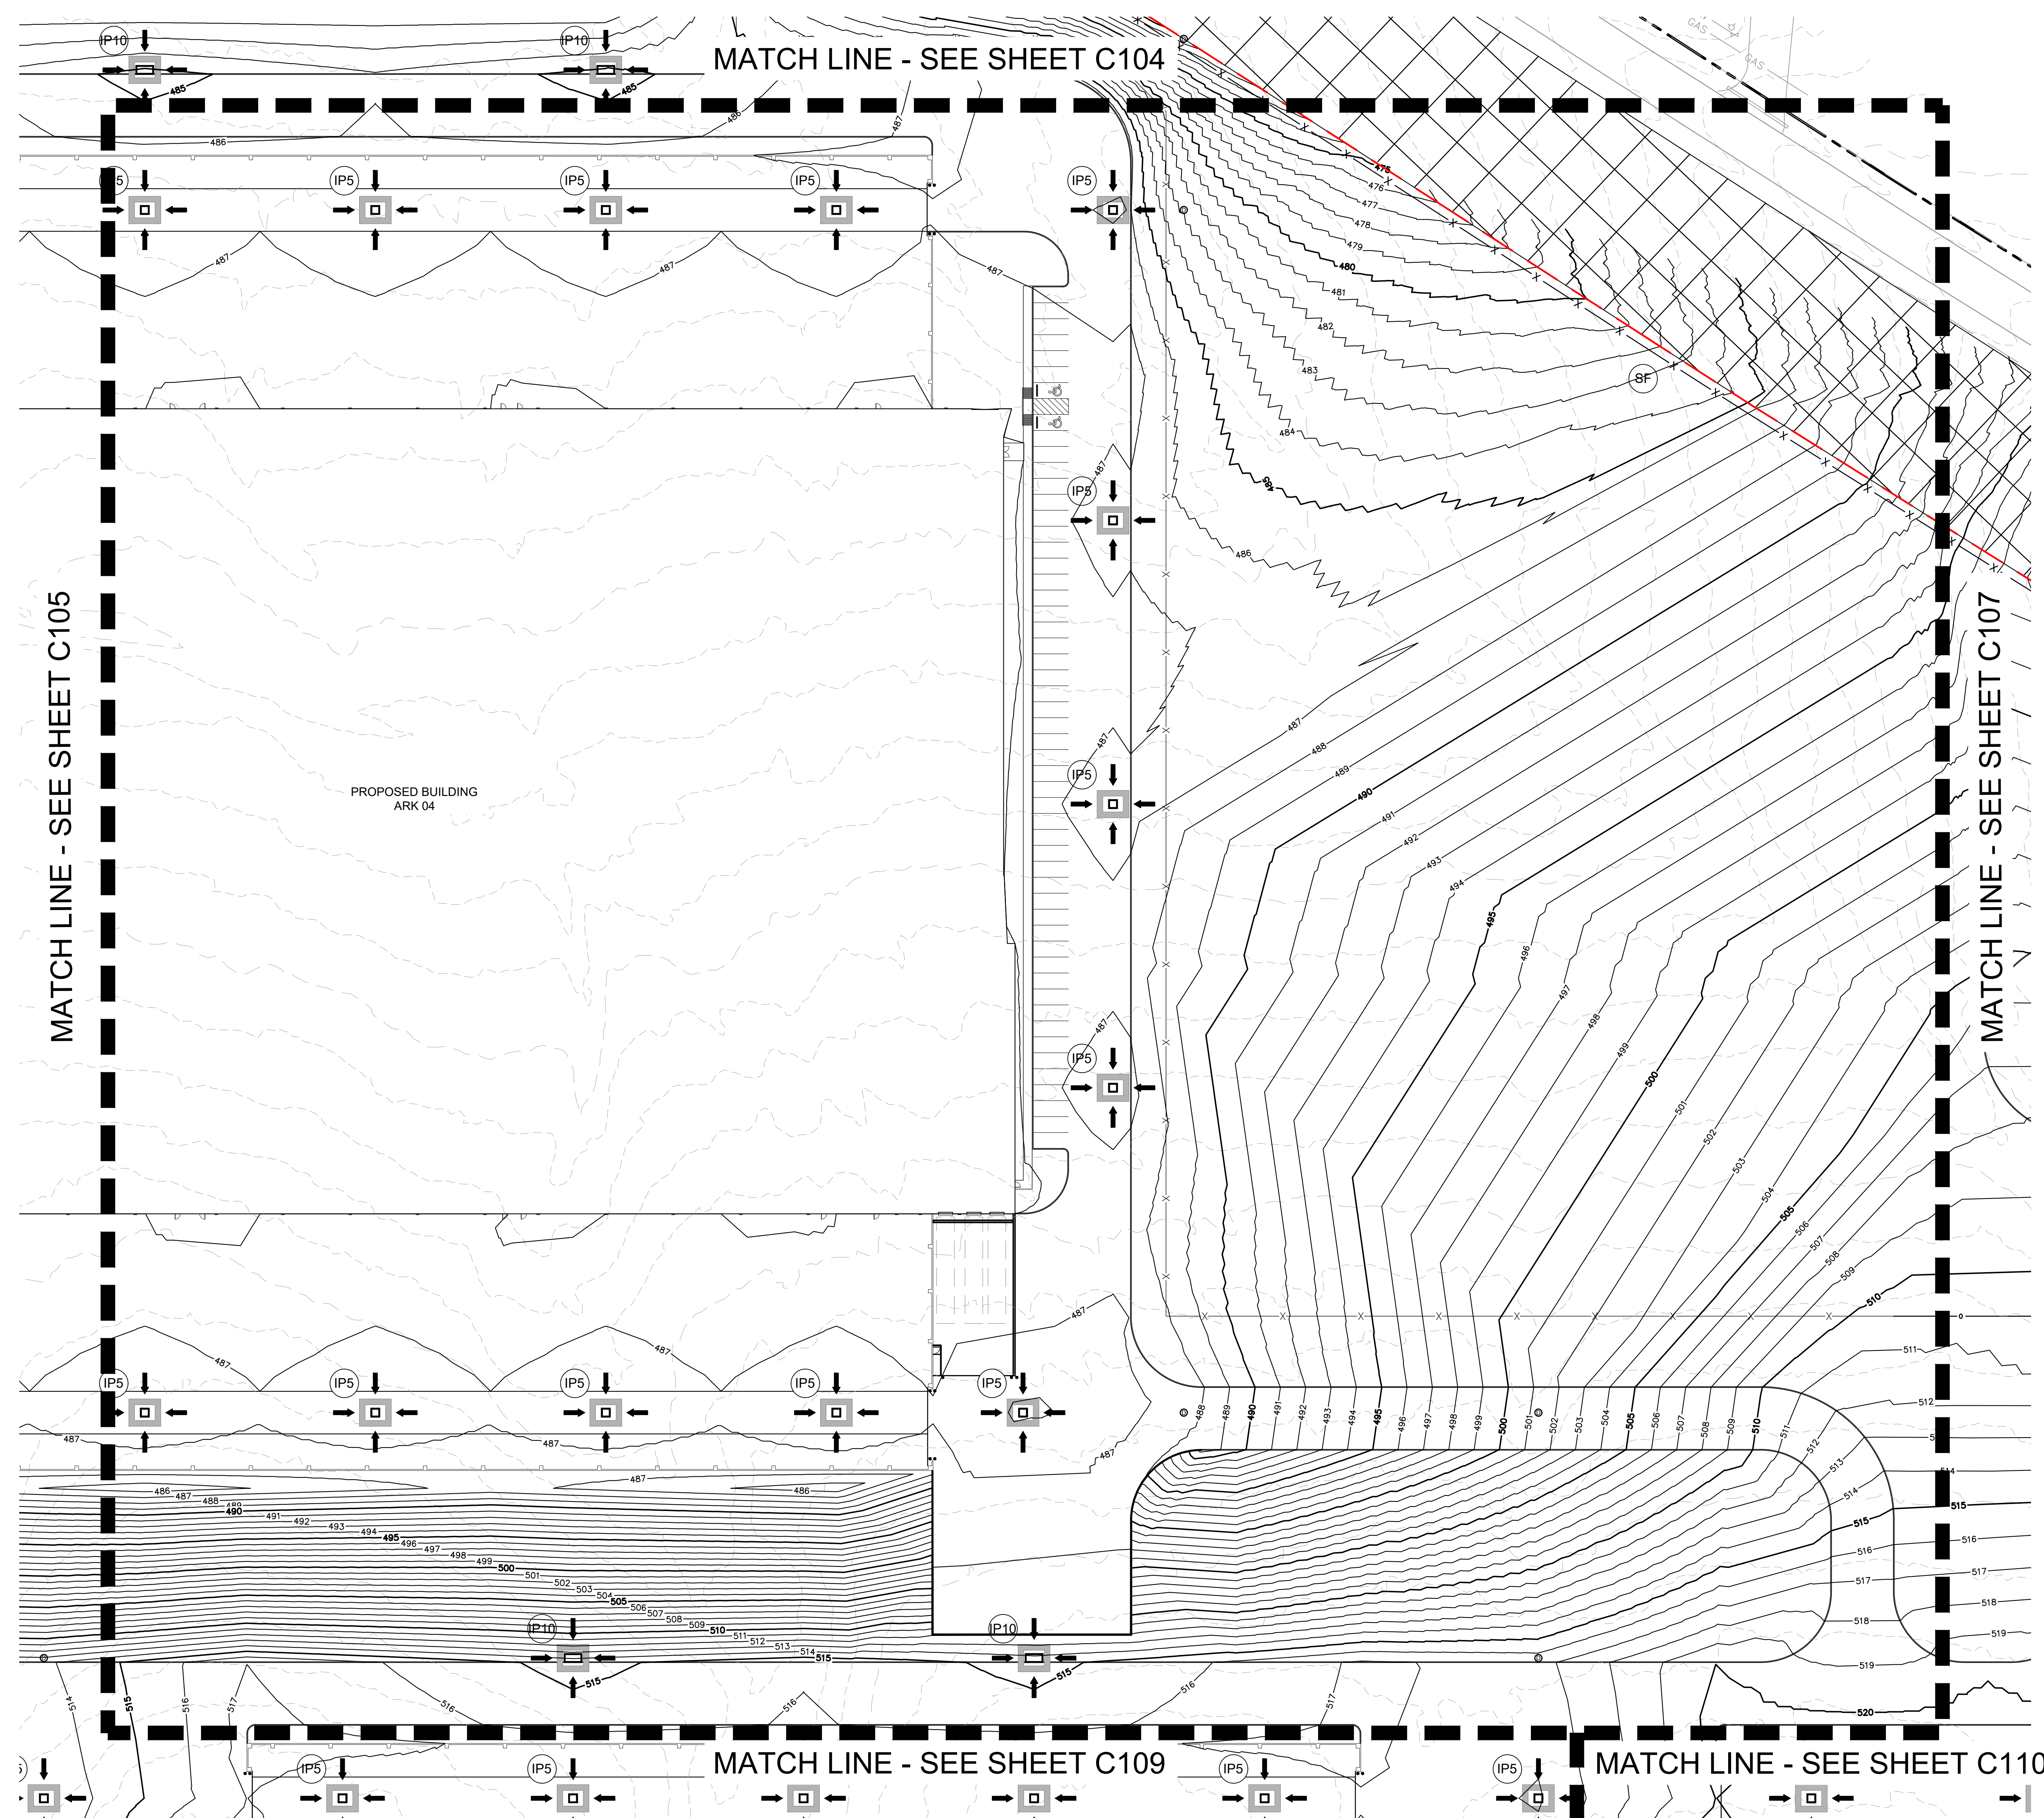

CAUTION!

EXISTING UNDERGROUND UTILITIES IN THE AREA
CONTRACTOR IS RESPONSIBLE FOR DETERMINING THE
HORIZONTAL AND VERTICAL LOCATION OF ALL UTILITIES
PRIOR TO CONSTRUCTION. CONTRACTOR SHALL BE
RESPONSIBLE FOR ANY REPAIRS TO EXISTING UTILITIES DUE
TO DAMAGE INCURRED DURING CONSTRUCTION.
CONTRACTOR SHALL NOTIFY THE ENGINEER OF ANY
DISCREPANCIES ON THE PLANS.

