

CHI St. Vincent LR MRI Replacement
RFQ Schedule
June 26, 2026

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	6/7	6/14	6/21	July	7/5	7/12	7/19	7/26	August	8/2	8/9	8/16	8/23	Se
1																				
2		Submit RFQ	1 day	Fri 6/26/26	Fri 6/26/26															
3		Project Award	1 day	Thu 7/2/26	Thu 7/2/26	2FS+3 days														
4		Precon/Assist with Design	39 days	Fri 7/3/26	Wed 8/26/26	3														
5		Cromwell Issue CD's	1 day	Thu 8/27/26	Thu 8/27/26	4														
6		Kinco Price CD's with subs	20 days	Fri 8/28/26	Thu 9/24/26	5														
7		Present GMP to CommonSpirit	1 day	Fri 9/25/26	Fri 9/25/26	6														
8		Negotiate GMP & Execute Contract	5 days	Mon 9/28/26	Fri 10/2/26	7														
9		CommonSpirit Issue PO	1 day	Mon 10/5/26	Mon 10/5/26	8														
10		Sign up Major Subs & PO's	1 day	Tue 10/6/26	Tue 10/6/26	9														
11		Submittals/Shop Drawings	25 days	Tue 10/6/26	Mon 11/9/26	10SS														
12		Release Long Lead Items	1 day	Tue 11/10/26	Tue 11/10/26	11														
13		Notice to Proceed	1 day	Mon 8/3/26	Mon 8/3/26															
14		ICRA Meeting with Hospital	1 day	Thu 10/29/26	Thu 10/29/26	13FS+62 days														
15		Set-up Containment for Existing MRI Removal	1 day	Fri 10/30/26	Fri 10/30/26	14														
16		Demolish and remove existing gypsum board wall, doors, door frames	3 days	Mon 11/2/26	Wed 11/4/26	15														
17		Install Temp/Permanent Shoring (structural framing) at existing load-bearing CMU wall	5 days	Thu 11/5/26	Wed 11/11/26	16														
18		Remove two sets of Double doors and frame in hallway	1 day	Mon 11/2/26	Mon 11/2/26	15														
19		Build Temp secure exterior enclosure with lockable door and remove existing storefront doors	2 days	Tue 11/10/26	Wed 11/11/26	16FS+3 days														
20		Remove existing CMU as required for removal of existing MRI machine	2 days	Thu 11/12/26	Fri 11/13/26	17														
21		Remove Existing MRI Machine	1 day	Mon 11/16/26	Mon 11/16/26	20														
22		Demolish and remove existing ceiling grid, ceiling tile, casework, gypsum board walls and floors	3 days	Tue 11/17/26	Thu 11/19/26	21														
23		Demolish and remove existing MEP in Mechanical Room	5 days	Mon 11/16/26	Fri 11/20/26	21FS-1 day														
24		Tie onto existing Chilled Water loop and bring into Mechanical Room	15 days	Mon 11/9/26	Fri 11/27/26	23FS-10 days														
25		Install and make final tie-ins for electrical in Mechanical Room	15 days	Mon 11/30/26	Fri 12/18/26	24														

Project: CHI St. Vincent MRI Re
Date: Wed 7/1/26

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

CHI St. Vincent LR MRI Replacement
RFQ Schedule
June 26, 2026

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	July							August							September			
								6/7	6/14	6/21	6/28	7/5	7/12	7/19	7/26	8/2	8/9	8/16	8/23						
26			Repair Shielding issues at RF Window Frame and RF Door Frame	2 days	Fri 11/20/26	Mon 11/23/26	22																		
27			Install RF Shielding at Walls as needed	3 days	Fri 11/20/26	Tue 11/24/26	22																		
28			Repair and Paint walls with first coat	5 days	Wed 11/25/26	Tue 12/1/26	27																		
29			Install ceiling grid (reset grilles & lights)	2 days	Wed 12/2/26	Thu 12/3/26	28																		
30			Install new floors	2 days	Fri 12/4/26	Mon 12/7/26	29																		
31			Install new casework	9 days	Tue 12/8/26	Fri 12/18/26	30																		
32			Finish paint (except for wall opening where new MRI machine will be brought in)	1 day	Mon 12/21/26	Mon 12/21/26	31																		
33			Install new ceiling tiles	1 day	Tue 12/22/26	Tue 12/22/26	32																		
34			Install New MRI Machine	1 day	Tue 1/19/27	Tue 1/19/27																			
35			Install Temp Containment Wall between MRI machine and wall opening)	1 day	Wed 1/20/27	Wed 1/20/27	34																		
36			Infill CMU wall with Metal Studs	1 day	Wed 1/20/27	Wed 1/20/27	35SS																		
37			Hang Sheetrock	1 day	Thu 1/21/27	Thu 1/21/27	36																		
38			Tape, float, paint sheetrock at former opening	4 days	Fri 1/22/27	Wed 1/27/27	37																		
39			Remove Temp Containment	1 day	Thu 1/28/27	Thu 1/28/27	38																		
40			Re-install Storefront and remove Temp Weatherproof, lockable barricade	3 days	Wed 1/20/27	Fri 1/22/27	34																		
41			Install new Double Door Frames (2 EA) and patch and re-finish and paint sheetrock	5 days	Wed 1/20/27	Tue 1/26/27	34																		
42			Hang 2 sets of double doors	1 day	Wed 1/27/27	Wed 1/27/27	41																		
43			Final Clean	2 days	Fri 1/29/27	Mon 2/1/27	39																		
44			Start-up of new MRI Machine	11 days	Mon 2/1/27	Mon 2/15/27																			
45			First Patient	1 day	Tue 2/16/27	Tue 2/16/27	44																		

Project: CHI St. Vincent MRI Re
Date: Wed 7/1/26

Task

Split

Milestone

Summary









Project Summary

Inactive Task

Inactive Milestone

Inactive Summary









Manual Task

Duration-only

Manual Summary Rollup

Manual Summary









Start-only

Finish-only

External Tasks

External Milestone









Deadline

Progress

Manual Progress











CHI St. Vincent LR MRI Replacement
RFQ Schedule
June 26, 2026

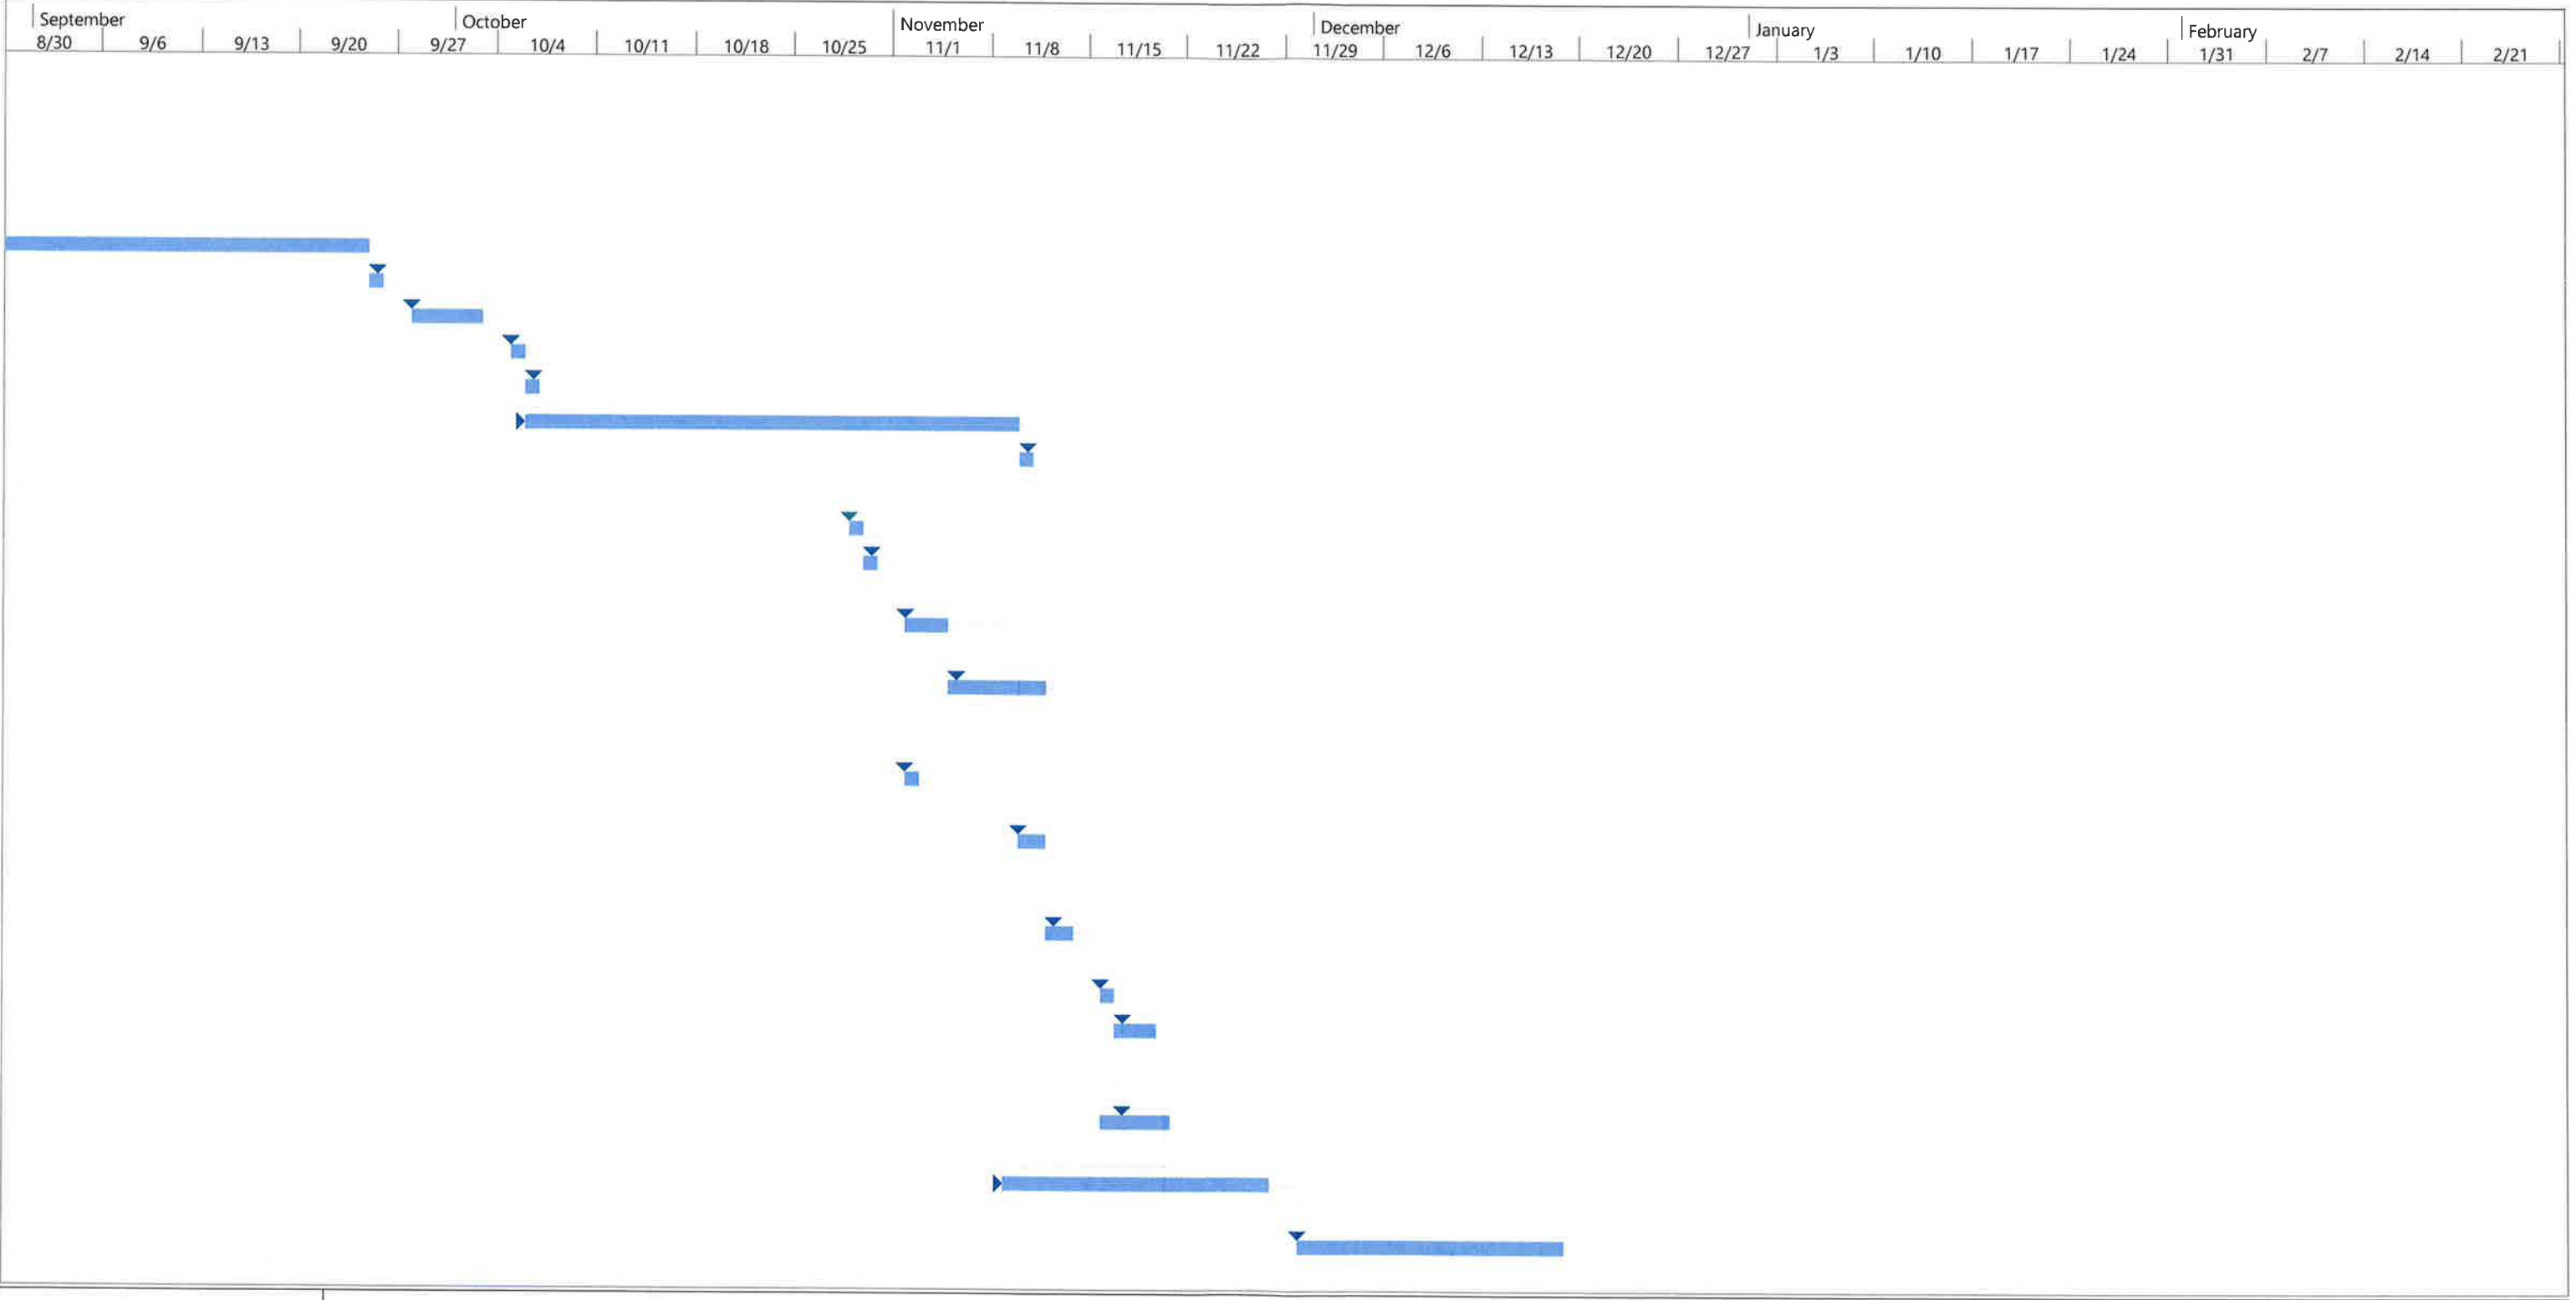

Project: CHI St. Vincent MRI Re Date: Wed 7/1/26	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

CHI St. Vincent LR MRI Replacement
RFQ Schedule
June 26, 2026

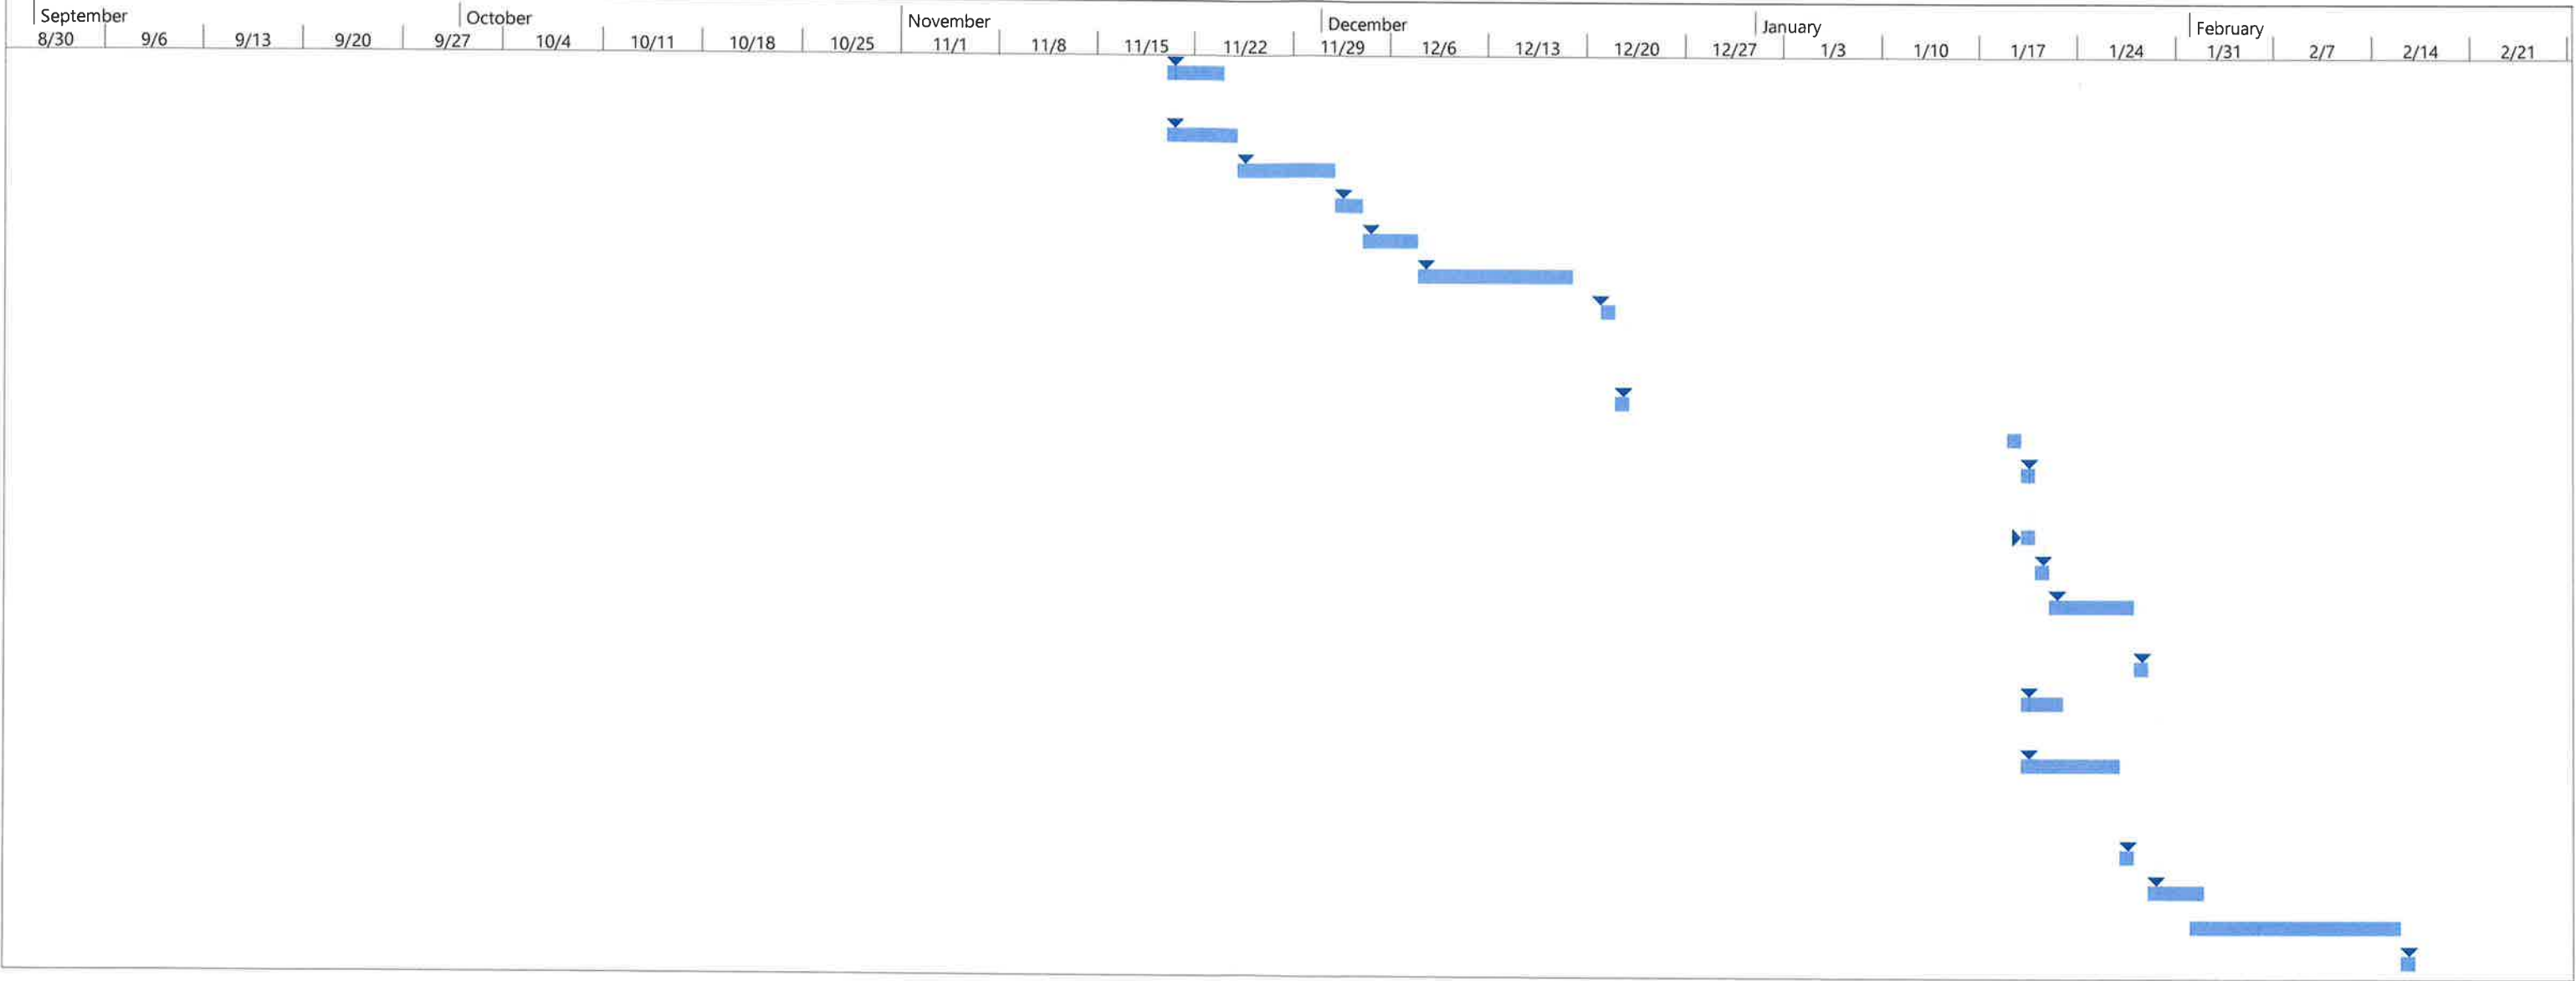

Project: CHI St. Vincent MRI Re Date: Wed 7/1/26	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
