

Quality People. Building Solutions.

Comfort Systems USA (Arkansas), Inc.
P.O. Box 16620
Little Rock, AR 72231
Phone 501-834-3320
Fax 501-834-5416

Date: 11/28/2023

Return Request: 12/5/2023

Project: MAC Building – 4th Floor

Supplier: Dollar Sheet Metal

Manufacturer: Various

Submittal: Air Terminal Units

Submittal Number: 23 36 00-01

Drawing # and Installation: Mechanical Drawings

ARCHITECT

Stocks Mann
401 W. Capitol, Suite 402
Little Rock, AR 72201
501-370-9207

ENGINEER

Insight
322 S. State Street, Suite 201
Little Rock, AR 72201
501-237-3077

GENERAL CONTRACTOR

Carson & Associates
1310 W. Daisy Bates Dr.
Little Rock, AR 72202
501-372-5816

MECHANICAL SUBCONTRACTOR

Comfort Systems USA (Arkansas), Inc.
9924 Landers Rd.
N. Little Rock, AR 72117
501-834-3320

Notes:


chowell@comfortar.com

9924 Landers Rd.
No. Little Rock, AR 72117

Submittal Drawing

Main Products

SDV

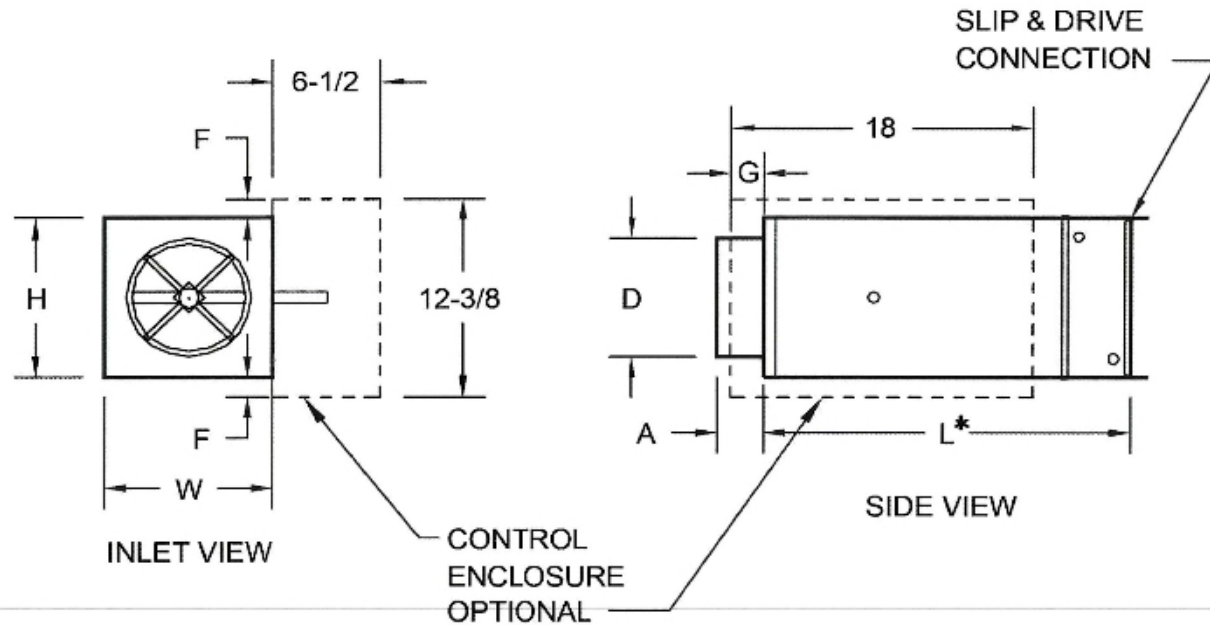

- SDV With Hot Water Coils
- Round Inlet Compatible With Nominal Rigid And Flex Duct Connections
- Slip And Drive Discharge Connection
- Patented Flo-Cross Multipoint Flo Sensor
- Damper Shaft With Delrin Bearings And Position Indicator
- Low Leakage Damper With Seal
- Right Or Left Hand Configurations Available (Right Hand Shown)

* Add 2-1/4 To Dim - L For 3 & 4 Row Coils

Dimensions are in inches, Product information subject to change without notice

| | | |
|---|----------------------------------|---|
| Project MAC BLDG 4TH FLR WHITE BOX RENOV | Submitted By: Shelly Wade | Date: 11-29-23 |
| Architect | Wade Company | SDV SDV - Single Duct Terminal Unit |
| Engineer | 708 Garland | |
| Contractor | Little Rock, Arkansas 72201 | |
| Version 1.0.00 | | |

Submittal Drawing

Main Products (continued)

| INLET SIZE | Dim - L | Dim - H | Dim - W | Dim - A | Dim - D | Dim - F | Dim - G |
|------------------------|---------|---------|---------|---------|---------|---------|---------|
| 10 - 0 OR 144-1400 CFM | 20-1/2 | 12-1/2 | 14 | 3-3/8 | 9-7/8 | - | 5-1/4 |
| 14 - 0 OR 302-3000 CFM | 23 | 17-1/2 | 20 | 3-3/8 | 13-7/8 | - | 3-1/4 |

OptionSchedule

| | |
|--|---|
| UNIT CONFIG 0 - STANDARD CONSTRUCTION LINER 1 - 1" DUAL DENSITY CASING OPTIONS CONST 0 - 22 GAUGE | DISCHARGE OPTIONS 0 - STANDARD RECTANGULAR CONTROL TYPE DFMT - ANALOG/DDC FIELD MOUNT ENCLOSURE HEAT W22 - LEFT HAND, 2-ROW, HOT WATER |
|--|---|

| ID | Quantity | Tag | CONTROLS DAMPER SIDE | INLET SIZE | MIN CFM | MAX CFM | AUX CFM | KW |
|----|----------|-----------|----------------------|------------------------|---------|---------|---------|----|
| 1 | 1 | ST-4B-100 | L - LEFT | 10 - 0 OR 144-1400 CFM | 275 | 500 | 275 | 0 |

| | |
|--|--|
| UNIT CONFIG 0 - STANDARD CONSTRUCTION LINER 1 - 1" DUAL DENSITY CASING OPTIONS CONST 0 - 22 GAUGE | DISCHARGE OPTIONS 0 - STANDARD RECTANGULAR CONTROL TYPE DFMT - ANALOG/DDC FIELD MOUNT ENCLOSURE HEAT W12 - RIGHT HAND, 2-ROW, HOT WATER |
|--|--|

| ID | Quantity | Tag | CONTROLS DAMPER SIDE | INLET SIZE | MIN CFM | MAX CFM | AUX CFM | KW |
|----|----------|-----------|----------------------|------------------------|---------|---------|---------|----|
| 2 | 1 | ST-4B-101 | R - RIGHT | 14 - 0 OR 302-3000 CFM | 908 | 1650 | 908 | 0 |

Dimensions are in inches, Product information subject to change without notice

| | | |
|--|--|--|
| Project MAC BLDG 4TH FLR WHITE BOX RENOV Architect Engineer Contractor Version 1.0.00 | Submitted By: Shelly Wade Wade Company 708 Garland Little Rock, Arkansas 72201 | Date: 11-29-23 SDV SDV - Single Duct Terminal Unit |
|--|--|--|
