Huntsville Sports Practice Facility
Preliminary Construction Schedule
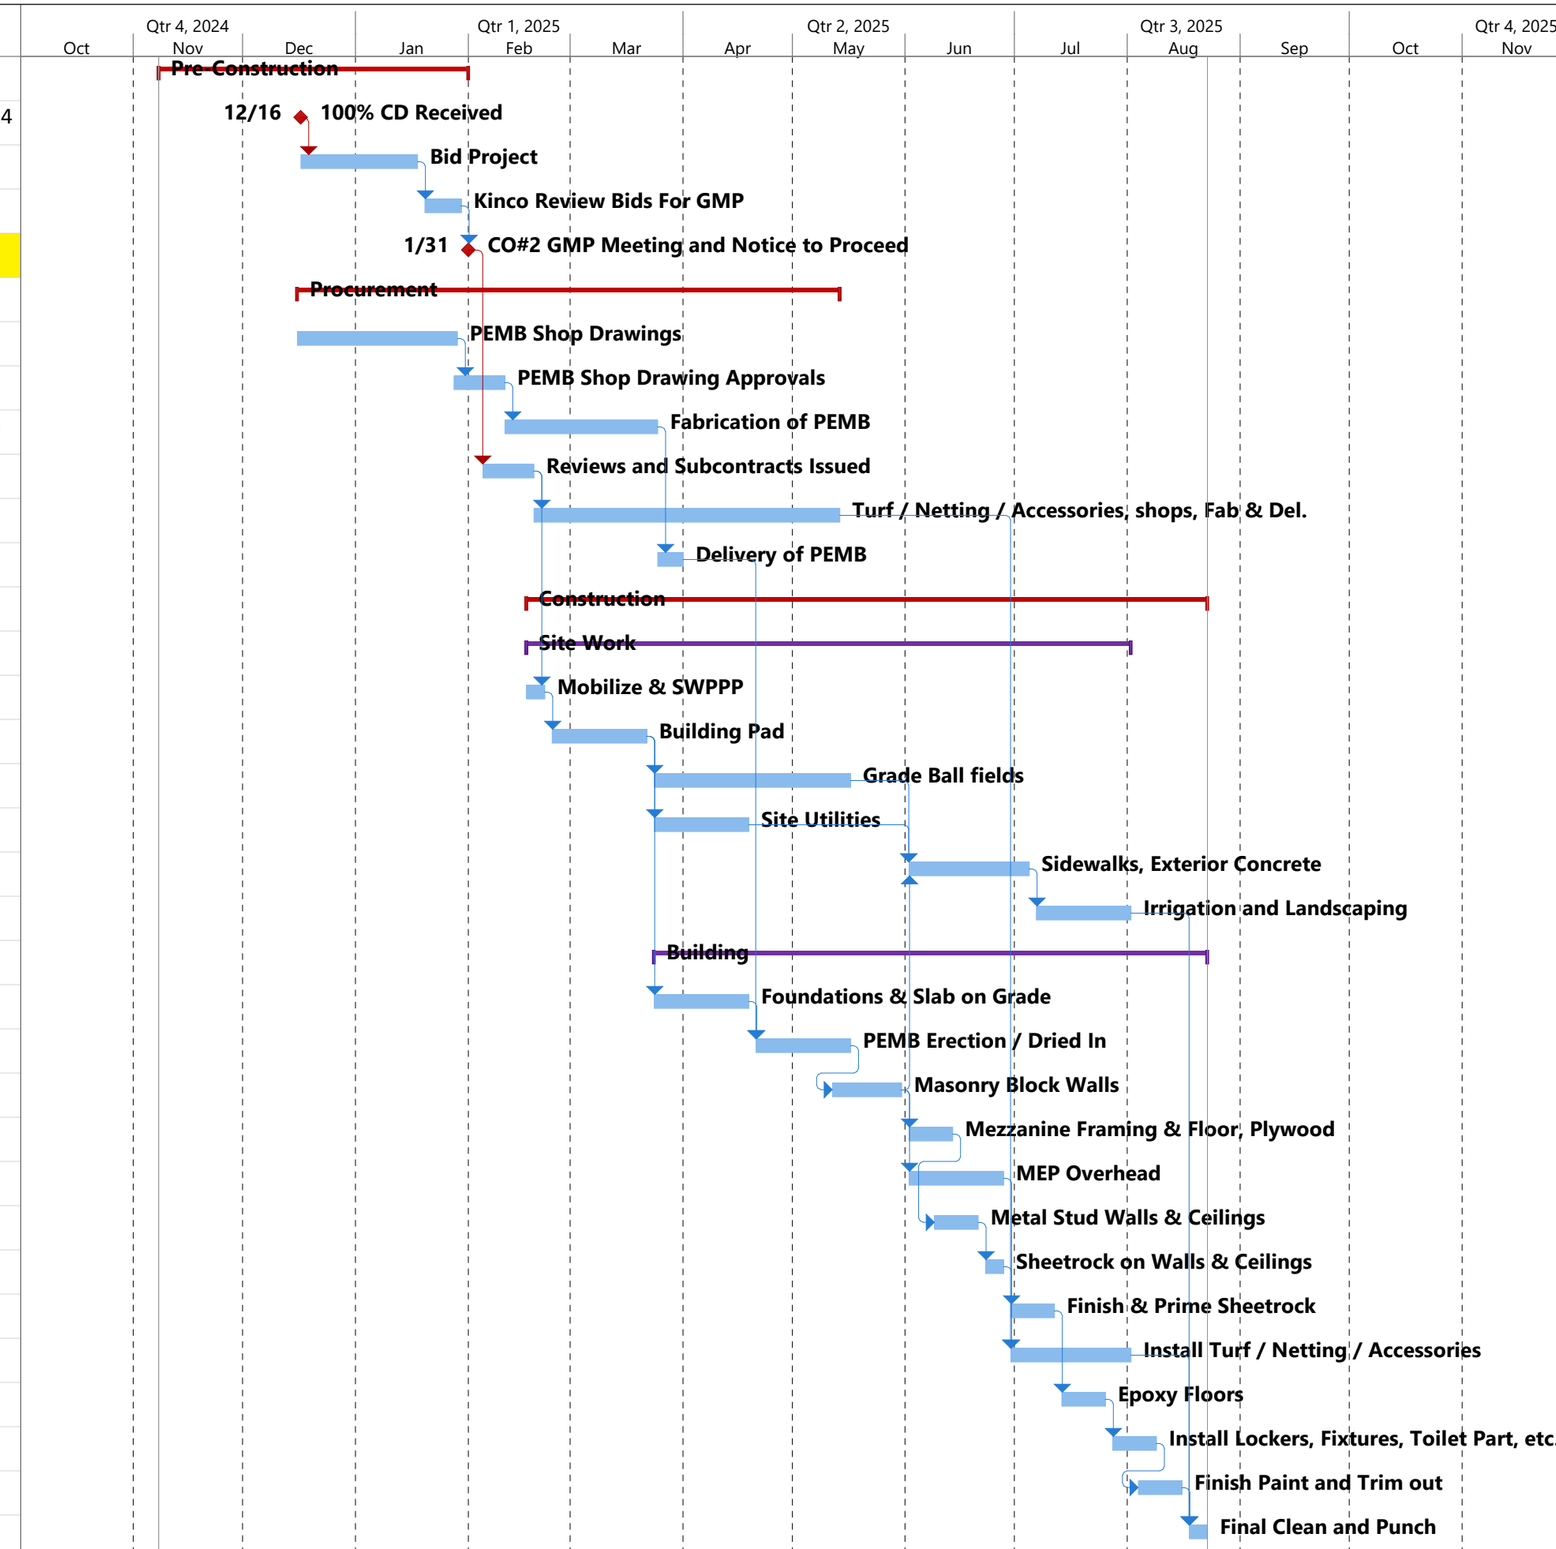
ID	Task Mode	Task Name	Duration	Start	Finish
1		**Pre-Construction**	**11.8 wks**	**Fri 11/8/24**	**Fri 1/31/25**
9		100% CD Received	1 day	Mon 12/16/24	Mon 12/16/24
6		Bid Project	4.4 wks	Tue 12/17/24	Fri 1/17/25
7		Kinco Review Bids For GMP	8 days	Mon 1/20/25	Wed 1/29/25
8		CO#2 GMP Meeting and Notice to Proceed	1 day	Fri 1/31/25	Fri 1/31/25
11		**Procurement**	**21 wks**	**Mon 12/16/24**	**Tue 5/13/25**
12		PEMB Shop Drawings	6 wks	Mon 12/16/24	Tue 1/28/25
13		PEMB Shop Drawing Approvals	2 wks	Tue 1/28/25	Mon 2/10/25
14		Fabrication of PEMB	6 wks	Tue 2/11/25	Mon 3/24/25
17		Reviews and Subcontracts Issued	2 wks	Wed 2/5/25	Tue 2/18/25
16		Turf / Netting / Accessories, shops, Fab & Del	12 wks	Wed 2/19/25	Tue 5/13/25
15		Delivery of PEMB	1 wk	Tue 3/25/25	Mon 3/31/25
18		**Construction**	**27 wks**	**Mon 2/17/25**	**Fri 8/22/25**
19		**Site Work**	**24 wks**	**Mon 2/17/25**	**Fri 8/1/25**
20		Mobilize & SWPPP	1 wk	Mon 2/17/25	Fri 2/21/25
25		Building Pad	4 wks	Mon 2/24/25	Fri 3/21/25
21		Grade Ball fields	8 wks	Mon 3/24/25	Fri 5/16/25
24		Site Utilities	4 wks	Mon 3/24/25	Fri 4/18/25
22		Sidewalks, Exterior Concrete	5 wks	Mon 6/2/25	Fri 7/4/25
23		Irrigation and Landscaping	4 wks	Mon 7/7/25	Fri 8/1/25
26		**Building**	**22 wks**	**Mon 3/24/25**	**Fri 8/22/25**
27		Foundations & Slab on Grade	4 wks	Mon 3/24/25	Fri 4/18/25
28		PEMB Erection / Dried In	4 wks	Mon 4/21/25	Fri 5/16/25
29		Masonry Block Walls	3 wks	Mon 5/12/25	Fri 5/30/25
30		Mezzanine Framing & Floor, Plywood	2 wks	Mon 6/2/25	Fri 6/13/25
37		MEP Overhead	4 wks	Mon 6/2/25	Fri 6/27/25
31		Metal Stud Walls & Ceilings	2 wks	Mon 6/9/25	Fri 6/20/25
36		Sheetrock on Walls & Ceilings	1 wk	Mon 6/23/25	Fri 6/27/25
35		Finish & Prime Sheetrock	2 wks	Mon 6/30/25	Fri 7/11/25
38		Install Turf / Netting / Accessories	5 wks	Mon 6/30/25	Fri 8/1/25
34		Epoxy Floors	2 wks	Mon 7/14/25	Fri 7/25/25
32		Install Lockers, Fixtures, Toilet Part, etc.	2 wks	Mon 7/28/25	Fri 8/8/25
33		Finish Paint and Trim out	2 wks	Mon 8/4/25	Fri 8/15/25
39		Final Clean and Punch	1 wk	Mon 8/18/25	Fri 8/22/25
