Print Date: 8-Aug-24

Activity ID	Activity Name	Orig. Dur.	Start	Finish
RSAF Facility Renovations for F-16 and F-35		666	6-Sep-24	31-Mar-27
Summary		666	6-Sep-24	31-Mar-27
GEN-530	Submit Proposal	0	6-Sep-24*	
GEN-540	90 days to review all proposals and award	90	6-Sep-24	4-Dec-24
GEN-490	NTP	0	5-Dec-24	
GEN-430	Design Duration	92	8-Jan-25	15-May-25
GEN-510	Obtain Permits	0	24-Jan-25	
GEN-520	Construction Start	0	24-Jan-25	
GEN-350	216 Bldg Duration	316	24-Jan-25	10-Apr-26
GEN-100	201 Bldg Duration	341	4-Apr-25	24-Jul-26
GEN-310	202 Bldg Duration	345	13-Jun-25	8-Oct-26
GEN-300	214 Bldg Duration	359	22-Aug-25	6-Jan-27
GEN-410	218 Bldg Duration	369	31-Oct-25	31-Mar-27
GEn-415	90 Days Window Prior to Final Completion	90	1-Jan-27	31-Mar-27
GEN-290	Demobilize	16	10-Mar-27	31-Mar-27
GEN-500	Project Complete	0		31-Mar-27
Construction Milestones		598	12-Dec-24	31-Mar-27
Preconstruction		513	5-Dec-24	26-Nov-26
Architect - Design		190	5-Dec-24	30-Aug-25
Submittals/Procurement		172	18-Feb-25	16-Oct-25
216 Building		89	18-Feb-25	23-Jun-25
201 Building		111	18-Mar-25	20-Aug-25
202 Building		111	18-Apr-25	19-Sep-25
214 Building		89	12-May-25	12-Sep-25
218 Building		89	16-Jun-25	16-Oct-25
Construction		569	24-Jan-25	31-Mar-27
216 Building (Renovate and restore to its original function the 17,500 SF)		316	24-Jan-25	10-Apr-26
Construction Activities FROM Proposal		316	24-Jan-25	10-Apr-26
Exterior/Skin		102	24-Jan-25	16-Jun-25
Interior		256	21-Feb-25	13-Feb-26
Project Closeout		40	16-Feb-26	10-Apr-26
201 Building (fire station repurposed as a storage fac. 9,563 SQF)		341	4-Apr-25	24-Jul-26
Construction Activities		341	4-Apr-25	24-Jul-26
Exterior/Building Skin		110	4-Apr-25	4-Sep-25
Interior		281	2-May-25	29-May-26
Closeout		45	25-May-26	24-Jul-26
202 Building (Repair and renovate facility to restore the original function as an aircraft		345	13-Jun-25	8-Oct-26
Construction Activities FROM Proposal		345	13-Jun-25	8-Oct-26
Exterior/Skin		15	13-Jun-25	3-Jul-25
Interior		305	13-Jun-25	13-Aug-26
Closeout		40	14-Aug-26	8-Oct-26
214 Building (Repurposed to an engine repair shop - 12,962 SF)		359	22-Aug-25	6-Jan-27
Construction Activities FROM Proposal		359	22-Aug-25	6-Jan-27
Exterior/Skin		110	22-Aug-25	22-Jan-26
Interior		304	12-Sep-25	11-Nov-26
Project Closeout		40	12-Nov-26	6-Jan-27
218 Building (The facility will be extensively repaired and renovated)		369	31-Oct-25	31-Mar-27
Construction Activities FROM Proposal		369	31-Oct-25	31-Mar-27
Exterior/Skin		115	31-Oct-25	9-Apr-26
Construct a new 972 square foot facility expansion		80	21-Nov-25	12-Mar-26
Interior		314	21-Nov-25	3-Feb-27
Project Closeout		40	4-Feb-27	31-Mar-27

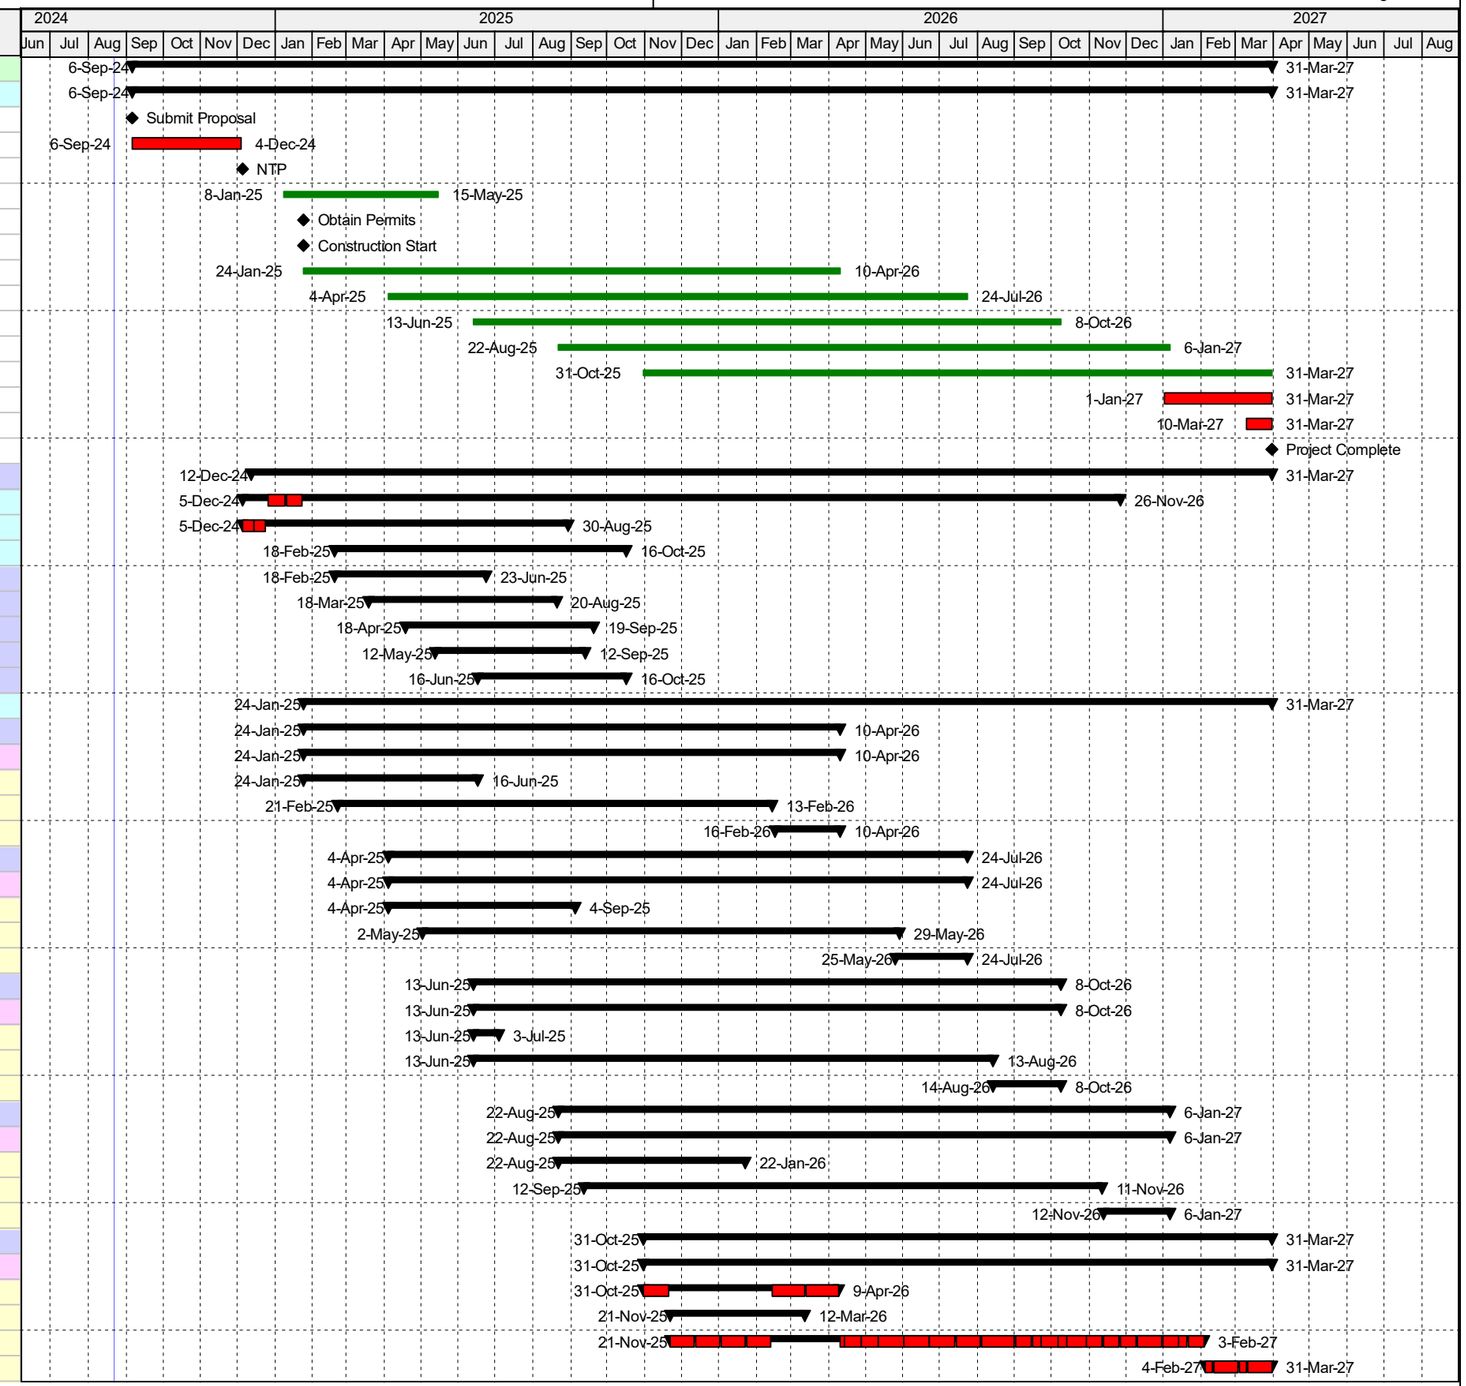

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | ◆ Milestone

RSAF Facility Renovations for F-16 and F-35

YATES CONSTRUCTION
